

Arbconsultants Ltd

Arboricultural Implication Assessment (AIA)



Arbconsultants Ltd

Consultants in Urban Forestry, Arboriculture and Environmental Sciences

Address	121 Station Road Hibaldstow		
Client	Mr P Fox	Client Ref	JEM Management Services
ARB Ref	EMB0317 / 4927	Consultant	Christopher Raper
Report Date	4th September 2021	Quality Checked	JG
Technical Arboriculture Approved			

Arbconsultants Ltd
The Rural Business Centre, Myerscough College, Bilsborrow, Preston, Lancashire PR3 0RY
Tel: 07887 601123 Email: enquiries@arbconsultants.co.uk
Web: www.arbconsultants.co.uk

Table of Contents

1. Scope and Limitations of Report
2. Qualifications and Experience
3. Summary
4. BS 5837:2005 Survey
5. Grading Category and Recommended Tree Works
6. Tree Constraints Plan (TCP) – Calculated Root Protection Area (RPA)
7. Tree Protection Plan (TPP) Protective Barriers
8. Method Statements & Additional Precautions outside the exclusion zone
9. Supervision
10. Conclusions and Recommendations

Appendix 1 – Site Location

Appendix 2 - Tree Survey Data Table

Appendix 3 - Tree Survey Plan (TSP)

Appendix 4 - Tree Constraints Plan Radii (TCP)

Appendix 5 – Tree Protection Plan (TPP)

Appendix 6 – RPA Calculations

Appendix 7 - Proposed / Combined

1. Scope and Limitations of Report

- 1.1 This report has been commissioned by Mr J. Mumby of JEM Management Services on behalf of Mr P. Fox and the scope of the report reflects his instructions.
- 1.2 The scope of the report is limited to a visual inspection of the trees (VTA Visual Tree Assessment).
- 1.3 This report was prepared as a report of work instructed by client (as specified). Neither Arbconsultants Ltd nor any associated company, nor any of their employees, nor any of their contractors, subcontractors or their employees, makes any warranty, express or implied, or assumes any legal liability or responsibility for the accuracy, completeness, or any third party's use or the report and its findings. Reference herein to any specific commercial product, process, or service by trade name, trademark, manufacturer, or otherwise, does not necessarily constitute or imply its endorsement, recommendation, or favouring by Arbconsultants Ltd or any associated company. The views and opinions of authors expressed herein do not necessarily state or reflect those of Arbconsultants Ltd or any associated company. The content, layout and any supporting digital files associated with this report are subject to copyright owned by Arbconsultants Ltd. Exceptions to this are present where that copyright has been legally assigned to us by another party/ organisation. In addition Arbconsultants Ltd may utilise content generated under license. Reproduction, scanning, copying or distribution of this report in any form is prohibited without prior written agreement. Neither Arbconsultants Ltd nor any of its associated companies, sub-contractors or suppliers will be responsible or liable for any claim of loss or damage resulting from the third party use of the information contained within this report.
- 1.4 The brief is to appraise the trees in relation to the proposed development of the site in accordance with British Standard 5837:2012 'Trees in relation to Construction – Recommendations'. To prepare a clear set of report recommendations with supporting plans and data to facilitate consideration of the Arboricultural implications by the Local Planning Authority.
- 1.5 To consider the development proposals and identify areas where there are arboricultural issues and to recommend possible solutions.
- 1.6 To consider additional information supplied and identify arboricultural issues arising from this information and to recommend possible solutions.
- 1.7 This report is not a Tree Risk Management or a Hazard Analysis Report and its use as such is invalid.

- 1.8 The report refers to the condition of the trees and an assessment of the site on the day that the evaluation was undertaken. All tree inspections, unless specified, have been undertaken from ground level and using non-invasive techniques. Comments contained within the report on the condition and risk associated with any tree relate to the condition of the tree at the date and time of survey. Please note that the condition of trees is subject to change. This change may occur, but is not limited to biological and non-biological factors as well as mechanical/physical changes to conditions in the proximity of the tree. Trees should be inspected at intervals relative to identified site risks and in accordance with best Industry practice and guidance. Arbconsultants Ltd can provide further information on this matter if required.
- 1.9 Please note no statutory control checks have been undertaken (unless specified). Where tree surgery works have been identified these works are based on the assumption that planning is approved, no tree works should be undertaken prior to determination of this application without up to date confirmation of the Tree Preservation Order / Conservation Area Status of the vegetation. All works should be undertaken in accordance with the appropriate Duty of Care. This should include, for example, site specific risk assessments and due diligence inspections for the presence of protected species. Any comment relating to 3rd party trees has been made without full access to the tree(s). Should these trees have any detrimental impact on the proposed development we would advise you to instruct us to contact the 3rd party and undertake further inspection work. Due to the changing nature of trees and their site circumstances this report and any recommendations made are limited to a 1 year period. Any alteration to the application site or any development proposals could change the current circumstances and may invalidate this report and any recommendations made. Should this be the case this report will require revision to reflect the development proposals.
- 1.10 Trees are dynamic structures that can never be guaranteed 100% safe; even those in good condition can suffer damage under average conditions. Regular inspections can help to identify potential problems before they become acute.
- 1.11 A lack of recommended work does not imply that a tree is safe and likewise it should not be inferred that a tree will be made safe following the completion of any recommended work.
- 1.12 Trees dimensions were measured using a combination of a Haglof digital Clinometer, a Leica Disto Laser Rangefinder and a Fujikura Diameter tape. All instruments were used in accordance with appropriate user guides.
- 1.13 Decay detection if requested and used is undertaken using an IML Resistograph.
- 1.14 All data provided by the testing equipment has been verified according to the equipment manufacturer's instructions.

- 1.15 No soil samples were taken and no soils analysis was undertaken. Clay soils are prone to compaction during development with damage to soil structure potentially having a serious impact on tree health. The design of foundations near problematic tree species will also need to take into consideration subsidence risk. Further advice from the relevant experts on the specific soil properties can be sought as necessary.
- 1.16 Any legal description or information given to Arbconsultants Ltd is believed to be accurate.
- 1.17 Where solutions to arboricultural problems are specified which require the usage of a third party product e.g. no dig roadway construction. No liability is assumed for the performance or suitability of the product and specialist advice as to the suitability or installation of the product should be sought from the manufacturer or other specialist.
- 1.18 This report is primarily an arboricultural report. Whilst comments relating to matters involving built structures or soil data may appear, any opinion thus expressed should be viewed as qualified, and confirmation from an appropriately qualified professional sought. Such points are usually clearly identified within the body of the report. It is not a full safety survey or subsidence risk assessment survey. These services can be provided but a further fee would be payable. Where matters of tree condition with a safety implication are noted during a survey they will of course appear in the report. No responsibility is assumed by Arbconsultants Ltd for legal matters that may arise from this report, and the Consultant shall not be required to give testimony or to attend court unless additional contractual arrangements are made.
- 1.19 Any alteration or deletion from this report shall invalidate it as a whole.

2. **Qualifications and Experience**

- 2.1 My name is Christopher Raper and I am a Consultant practising through Arbconsultants Limited, which is an Arboricultural Consultancy Practice based at Myerscough College, Preston, Lancashire. The Practice Specialises in Arboriculture, Urban Forestry, Biological Sciences and Project Management.
- 2.2 I am a Consultant specialising in tree failure, hazard evaluation, risk assessment related to trees, planning and development where trees are involved and insurance claims where tree failure is involved and/or building damage occurs which may be attributed to the activity of trees. I have received extensive training in relation to trees, clay soils and subsidence of low-rise buildings. I am a specialist in the field of trees/vegetation and special construction engineering methodologies. I am familiar with different Tree Hazard Evaluation systems and conversant in Visual Tree Assessments (VTA) techniques.
- 2.3 I have a 1st class honours degree in Arboriculture awarded by Myerscough College in conjunction with the University of Central Lancashire. I have over 20 years experience in the Arboricultural industry ranging from Tree Officer with a Local Authority through to Senior Consulting level with an Arboricultural Consultancy. I have provided guest lectures on Arboricultural Consultancy to the MSc course on Arboriculture and Urban Forestry and taught the Planning and Law modules to the BSC Hons course run by the University of Central Lancashire and Myerscough College. I have attended formal and informal public inquiries and have supplied consultancy advice as part of design, project management and consultant/legal teams.

3. Summary

- 3.1 The survey was carried out on land adjacent 121 Station Road Hibaldstow. The survey area comprises the garden area of the above property. The area is bounded to the East by Station Road and to the west by a haulage yard. Tree stock within the site is as described in Appendix 2 and as shown on the tree survey plan at Appendix 3.
- 3.1 We have not been supplied with detailed drawings showing foundation types etc therefore we have made certain assumptions and have supplied method - statements that will cover most contingencies whereby the development may impact upon the trees. If necessary these method statements can be modified once full technical drawings have been produced.
- 3.2 We understand that the site is not subject to Conservation Area Notification and we are not aware of any Tree Preservation Orders within the surveyed area. The status of all the trees on site would need to be confirmed prior to any works being undertaken on the surveyed trees, as listed in Appendix 2 Tree Data.

4. **BS: 5837:2012 'Trees in relation to construction – Recommendations'**

4.1 The trees on site have been surveyed in accordance with BS5837:2012 'Trees in relation to construction – Recommendations'.

4.2 The survey lists all the trees or groups of trees (excluding those trees already scheduled for removal) that may be impacted upon by the development and will include the following information.

- Reference number (to be recorded on the tree survey plan)
- Species
- Height in metres.
- Stem diameter at 1.5m above adjacent ground level (on sloping ground to be taken on the upslope side of the tree base) as per annex D of the Standard or
 - a) For trees with two to five stems, the combined stem diameter should be calculated as follows: $\sqrt{(\text{stem diameter } 1)^2 + (\text{stem diameter } 2)^2 + (\text{stem diameter } 5)^2}$
 - b) For trees with more than five stems (not illustrated in Annex C), the combined stem diameter should be calculated as follows:
 $\sqrt{(\text{mean stem diameter})^2 \times \text{number of stems}}$
- Branch spread in meters taken at the four cardinal points to derive an accurate representation of the crown (to be recorded on the tree survey plan).
- Existing height above ground level of first significant branch and direction of growth (e.g. 2.4-N) of the canopy, to inform on ground clearance, crown/stem ratio and shading;
- Life stage (e.g. young, semi-mature, early mature, mature, over-mature).
- General observations, particularly of structural and/or physiological condition (e.g. the presence of any decay and physical defect), and/or preliminary management recommendations;
- Estimated remaining contribution, in years (<10, 10+, 20+, 40+).
- Category U or A to C grading (see 4.5 and Tables 1 and 2), to be recorded on the tree survey plan.

4.3 The survey data is attached at **Appendix 2** of this report.

4.4 The British Standard at 5.5.6 states that the following factors need to be considered -

- a) **site construction access;** this should be via the access through the boundary from the highway.
- b) **the intensity and nature of the construction activity;** the construction will be of medium intensity. The site compound should be outside all root protection areas.
- c) **contractors' car parking;** Contractors will be expected to use off-street parking on the development.
- d) **phasing of construction works;** all tree works will be completed and protective barriers and ground protection will be in place prior to any construction work -

5.0 Grading Category and Recommended Tree Works

5.1 Trees that have the potential to be affected by the development have been classified according to BS5837:2012 and the data and categorisation relating to trees that may affect the development is contained at Appendix 2.

5.2 Category "A" Trees are classified as high quality and value in such condition as to make a substantial contribution for a minimum of 40 years. Trees T6 and T31 would be categorised as A.

5.3 Category "B" i.e. those of moderate quality and value: those in such a condition as to make a significant contribution (a minimum of 20 years is suggested). Category B Trees are defined as trees that might be included in the high category, but are downgraded because of impaired condition (e.g. presence of remediable defects including unsympathetic past management and minor storm damage). There were fifteen trees on or adjacent to the site that would fall into the B category (Trees T1 - T5 T7 - 9 T14, T16, T19, T21, T22 and T39).

5.4 Trees that have been classified as Category "C" are of lower quality and value; currently in adequate condition which could if necessary remain until new planting is established, trees present in groups or woodlands, but without this conferring on them significantly greater landscape value. The majority of trees and hedges on and adjacent to the site are C category (Trees T11 to T13, T15, T17, G18, T20, T23 to T30, T32 to T38, T41 to T44 and Shrub Groups SG1 and SG2).

5.5 Category "C" trees may **not** usually be retained where they would impose a significant constraint on development.

5.6 Category "U" trees are those in such a condition that any existing value would be lost within 10 years and which should, in the current context, be removed for reasons of sound arboricultural management. Examples include...

- Trees that have a serious, irremediable, structural defect, such that their early loss is expected due to collapse, including those that will become unviable after removal of other U category trees (i.e. where, for whatever reason, the loss of companion shelter cannot be mitigated by pruning).
- Trees that are dead or showing signs of significant, immediate, and irreversible overall decline.
- Trees infected with pathogens of significance to the health and/or safety of other trees nearby (e.g. Dutch elm disease), or very low quality trees suppressing adjacent trees of better quality.

Trees T10 and T40 would be categorised as U.

5.7 Trees T23 to T26, T33, T34 and T41 to T44, all category C trees should be felled to facilitate development. All trees that are to be left in situ should be protected in accordance with the method statements contained within this report.

5.8 Permissions: Under no circumstances is any tree work to be instigated without having first checked with the Local Planning Authority that no statutory controls

apply in respect of the trees. All tree workers shall have the relevant NPTC qualifications and shall submit completed risk assessments to the project manager prior to commencement of tree-work.

- 5.9 All pruning shall be done in accordance with the principles of 'Natural Target Pruning' and in accordance with the current relevant British Standard, **BS3998: 2010** 'Recommendations for Tree Work'. All pruned sections shall be lowered to the ground in a controlled manner such that no damage is done to other trees or vegetation and structures beneath. The implication of tree works must have regard to the presence of any nesting Birds or Bats and their roosts, which are protected under the Wildlife and Countryside Act 1981

6.0 Tree Constraints – Calculated Root Protection Area (RPA)

- 6.1 BS5837 (2012) requires that the root protection area is calculated for each of the retained trees on the development. The root protection area is the minimum area in m² which should be left undisturbed around each retained tree. The RPA should be calculated using Annex D of the Standard as an area equivalent to a circle with a radius 12 times the diameter calculated for the stem of the tree.
- 6.2 The standard calculated RPA's and the protection zone radii are detailed at Appendix 6 of this report.
- 6.3 The RPA, for each tree as determined in Table 2 of the standard, should be plotted on the **Tree Constraints Plan** taking full account of the following factors, as assessed by an arboriculturalist, which may change its shape but not reduce its area whilst still providing adequate protection for the root system.
- a) The likely tolerance of the tree to root disturbance or damage, based on factors such as species, age and condition and presence of other trees.
 - b) The morphology and disposition of the roots, when known to be influenced by past or existing site conditions (e.g. the presence of roads, structures and underground services).
 - c) The soil type and structure.
 - d) Topography and drainage.

7.0 Arboricultural Method Statement - Tree Protection Plan (TPP) Barriers

- 7.1 To enable the development progress without causing damage to the retained trees in situ exclusion zones need to be maintained. The exclusion zones (Construction Free Zone) as defined in this report will be protected with fencing. The fencing is to be strong enough to resist impacts and suitable to the degree of construction activity on the site and to be in accordance with that specified of BS5837:2012.
- 7.2 All fencing will be in place prior to any other development work (with the exception of necessary tree works) commencing on site. Such fencing will therefore be erected before any materials or machinery is brought onto site. Once erected the fences will not be moved or altered in any way without prior consultation with the Local Planning Authority other than for operations detailed in this report. If the fencing is damaged in any way it will be re-instated to its original condition before construction work can re-commence Notices will be erected on the fencing stating Protected Area – No Operations within Fenced Area. Protective fences shall be maintained in situ until all equipment, machinery and surplus materials have been removed from the site. No vehicle shall access shall be allowed within the construction frees zone. Nothing will be stored or placed in any area fenced in accordance with this condition and the ground levels within those areas shall not be altered, nor shall any excavation be made other than those detailed in this report, without the written consent of the Local Planning Authority.
- 7.3 The total exclusion zones are marked on the accompanying drawing in Appendix 5 (**Tree Protection Plan**). British Standard 5837:2012 (Appendix 6) indicates the recommended areas for the Root Protection Areas (RPA) which should be enforced with protective fencing. Specifications within BS5837-2012 inform our recommendations for both the fencing type as detailed below in figure 2 and the location of this fencing. As detailed in section 6.2.3.1 of the standard it is acceptable for the barriers to be set back and ground protection to be put in place.
- 7.4 Barriers should be fit for purpose and appropriate to the degree of activity and proximity of work to the retained trees. All protective fencing is to be constructed in accordance with BS:5837(2012) – Figures 2 and 3 specification reproduced below.

Figure 3 Examples of above-ground stabilizing systems


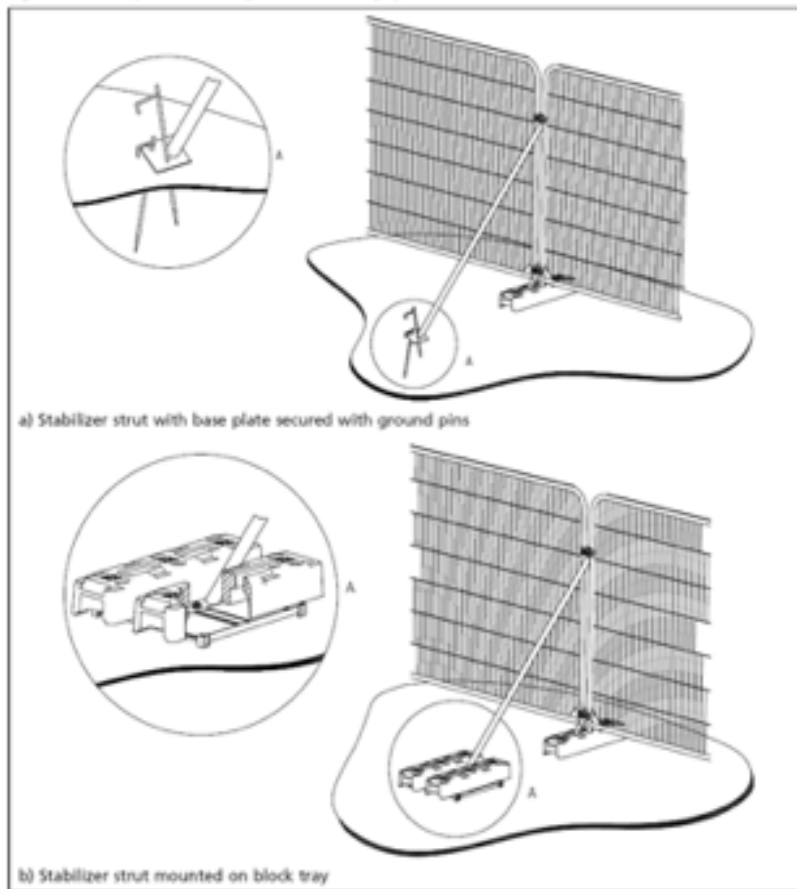


Figure 2 Default specification for protective barrier

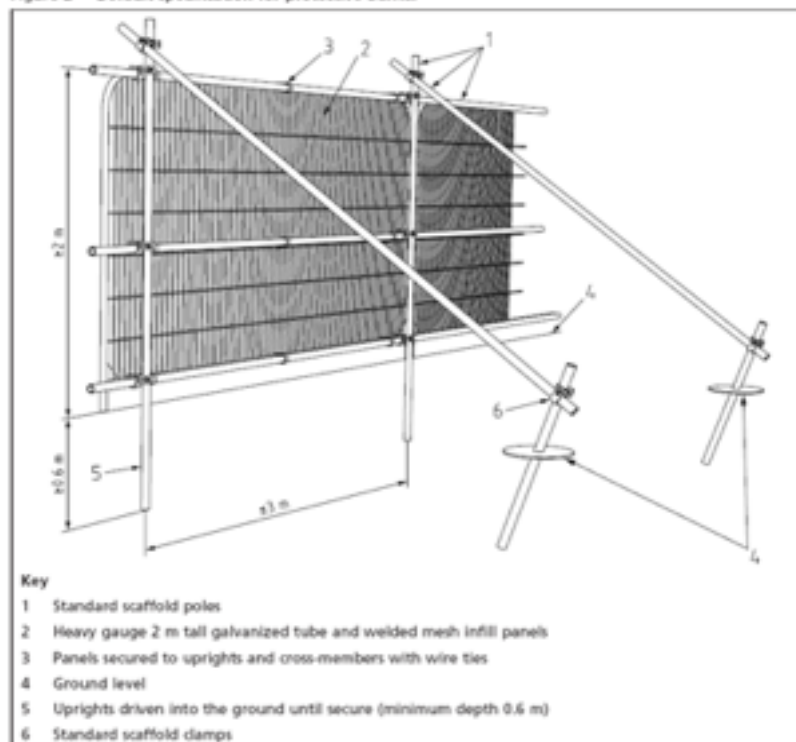

8.0 Installation of Services (Underground and above ground services)

- 8.1 Trenching for the installation of underground services severs any roots present and may change the local soil hydrology in a way that adversely affects the health of the tree. For this reason particular care should be taken in the routing and methods of installation of underground services and where possible routing the services outside the specified RPA's
- 8.2 At all times where services are to pass within the RPA, detailed plans showing the proposed routing should be drawn up in conjunction with an Arboriculturist. Such plans should also show the levels and access space needed for installing the services. A decision on either directional drilling / micro-tunnelling / impact moling should be taken using Table 3 of BS5837 2012 as a guide.

Table 3 Trenchless solutions for differing utility apparatus installation requirements

Method	Accuracy	Bore dia. ^{A)}	Max. sub. ^{B)} length	Applications	Not suitable for
	mm	mm	m		
Microtunnelling	<20	100 to 300	40	Gravity-fall pipes, deep apparatus, watercourse/ roadway undercrossings	Low-cost projects due to relative expense
Surface-launched directional drilling	≈100	25 to 1 200	150	Pressure pipes, cables including fibre optic	Gravity-fall pipes, e.g. drains and sewers ^{C)}
Pipe ramming	≈150	150 to 2 000	70	Any large-bore pipes and ducts	Rocky and other heavily obstructed soils
Impact moling ^{D)}	≈50 ^{E)}	30 to 180 ^{F)}	40	Gas, water and cable connections, e.g. from street to property	Any application that requires accuracy over distances in excess of 5 m

- 8.3 In this instance it is envisaged that there should be no necessity for any services to enter the root protection areas of retained trees but as it is unknown as to where the utilities will ultimately enter the site this method statement is for such an eventuality.
- 8.4 If it is found that there is a need for services to pass through Root Protection Areas Micro-tunnelling is the preferred method although it may be acceptable (where services need to pass through the RPA and a mole is unsuitable) to install the services in conjunction with the specification of NJUG 10. All excavations that are done in conjunction with the NJUG specification shall take place with an air-spade and any root pruning necessary will be undertaken by a qualified tree surgeon in accordance with both NUG 10 and BS3998 2010. The timing and extent of pruning (especially regarding the number and size of wounds; should be determined by both the management objectives and an assessment of the likely effects on the tree and its surroundings. The assessment should take account of species tolerances, the tree's age and condition and any implications for the safety of other trees. Any damaged roots should be cut so that the final wound is as small as possible and free from ragged torn ends. In the interests of clarity we only recommend this method of installing the cable if micro tunnelling, Impact moling or directional drilling cannot be accommodated.
- 8.5 Any roots which are to be left exposed for more than three hours should be covered in damp straw and/or hessian covers. Also note that if temperatures

exceed 16C the time should be reduced to one hour before roots should be protected.

- No pruning of roots over a diameter of 25mm should be undertaken unless permission of the Local Authority tree officer is given. *Any damaged roots should be cleaned and pruned back to an appropriate place*
- The existing top soil is to be retained where possible. Any voids or depressions within the ground surface are to be filled with sharp sand (not builders sand) to maintain levels.



8.6 Consideration will be given to the routing of above ground services in order to avoid the need for detrimental and repetitive pruning. In this regard the current and future crown size of the tree should be assessed.

8.7 Cellular Confinement System

8.8 It is envisaged that the proposed development will require a c e l l u l a r confinement construction for the driveway within the root protection areas of trees T29, T31, T32 and T39. This will enable T31 to be retained in a central position of the driveway. The Cellular Confinement System should be installed prior to any other construction activity on this site. The use of this system avoids the requirement for digging into the soil and damaging existing roots. Using this technology will avoid damaging the soil structure through compaction. Soil damage of this nature may disrupt the efficient exchange of water and gasses in and out of the soil and inhibit root growth. Mature and over-mature trees are more vulnerable to disturbance of this nature when compared to younger trees. The use of a cellular confinement system reduces the bearing pressure on the subsoil by stabilising aggregate surfaces against rutting under pressure loads. Even one pass over soil by a vehicle compacts the soil. It is therefore crucial that the area that is to be covered with a cellular confinement system is protected from the beginning of construction works. As this surface will need to support regular vehicles and potentially fire engines a 150mm thick cellular confinement system will be required. These areas are shown at Appendix 5 tree protection plan and the following methodology is to be applied:

- The surface needs to be laid on flat ground and so first any debris, mulch and vegetation will need to be removed from the soil surface. Any major protrusions such as rocks should be carefully removed. This is to be done using hand tools only. Stumps are to be excavated out to just below ground level, again, using hand tools. Undertake pruning works as required.
- Any roots which are to be left exposed for more than three hours should be covered in damp straw and/or hessian covers. Also note that if temperatures exceed 16c this time should be reduced to one hour before roots should be protected.
- No pruning of roots over a diameter of 25mm should be undertaken unless permission of the Local Authority tree officer is given. Any damaged roots should be cleaned and pruned back to an appropriate place

- Apply translocated herbicide to area for driveway and remove dead vegetation with hand tools. The existing surface and top soil is to be retained. Any voids or depressions (including those formed by stump removal) within the ground surface are to be filled with sharp sand (not builders sand) to maintain levels.
- Once the surface is flat the area must be covered with a non woven geo-textile separation filtration layer over area for driveway and hard landscape that will prevent different mineral materials mixing while allowing water to pass through. If several sheets are required ensure that they overlap by at least 30cm;
- Install cellular confinement mats over the area. Expand the Cellweb or other proprietary brand panels to the full length. Trim to desired width with a craft knife. Pin the Cellweb panels with staking pins to anchor open the cells and staple adjacent panels together to create a continuous mattress. Increase number of staking pins from 10 per panel to 20 on any downward side of mattress to provide greater support for the section of the hard surface subject to camber. Install treated timber boarding for lateral support secured by robust stakes for both sides
- Infill the Cellweb with a clean no fines angular granular fill of size 40-20mm within This material is then compacted with the use of a smooth wheeled roller.
- Install second layer of geo textile separation filtration layer.
- The excavation needed for the placement of kerbs, edgings and their associated foundations and haunchings can damage tree roots. Within the RPA, this will be avoided either by the use of alternative methods of edge support. It is proposed to use a no dig option such as pinned sleepers or pinned kerb edging. The final specification will be defined by the project architect. Where it is necessary to pin kerbing in place, the pins should, where practical, be located clear of any major tree roots visible on the surface.
- Finally a surface layer is applied; this must be porous. 'No dig' construction is accomplished through the use of a perforated cellular confinement system in the sub-base layer. Cellular confinement systems reduce the overall depth of construction by introducing a cellular structure which dissipates downward loads by a horizontal transfer through the cell structure. This process in conjunction with the perforated cell wall also imports structural integrity to free draining aggregates which would otherwise be unacceptable in road construction. Therefore, a robust, shallow and free-draining sub-base is achieved, which allows access whilst allowing water and oxygen to permeate down to the tree roots.

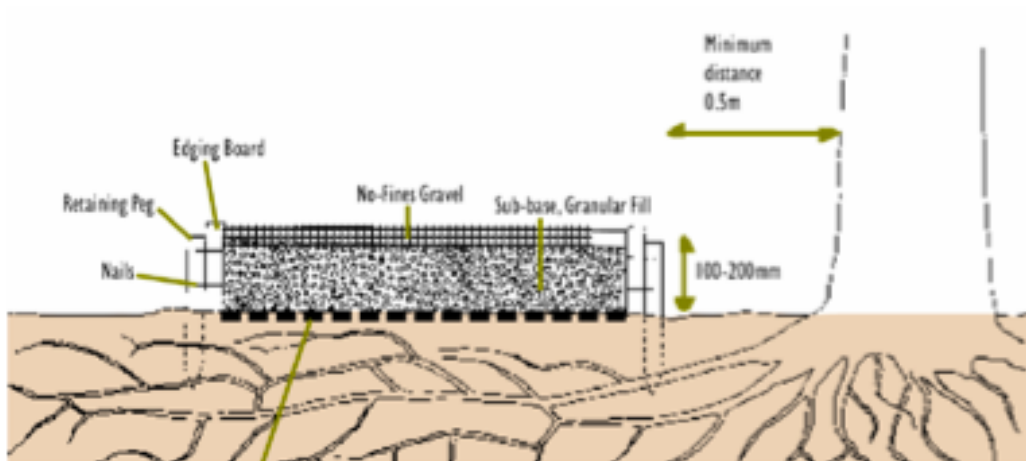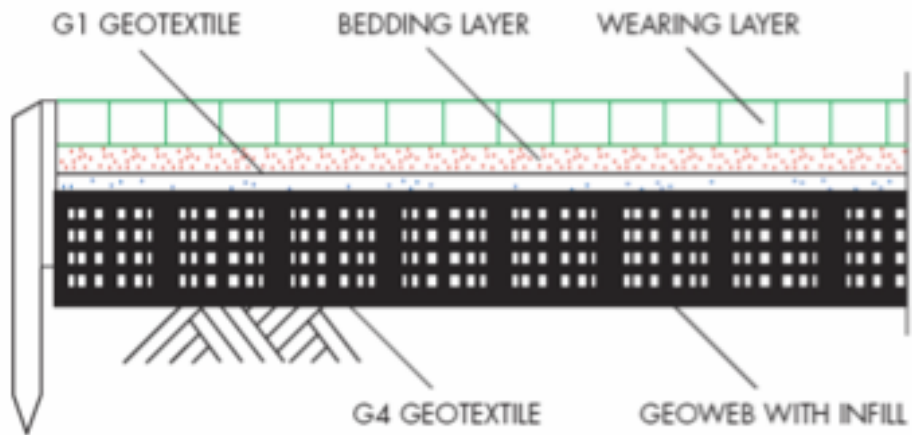

Cellular Confinement System

8.9 Additional precautions outside the exclusion zone :-

8.10 Once the exclusion zone has been protected by barriers and/or ground protection, construction work can commence. All weather notices should be erected on the barrier with words such as: **“Construction exclusion zone — Keep Out”**.

8.11 In addition the following should be addressed or avoided.

- a) Care should be taken when planning site operations to ensure that wide or tall loads, or plant with booms, jibs and counterweights can operate without coming into contact with retained trees. Such contact can result in serious damage to them and might make their safe retention impossible. Consequently, any transit or traverse of plant in close proximity to trees should be conducted under the supervision of a banks-man to ensure that adequate clearance from trees is maintained at all times. In some circumstances it may be impossible to maintain adequate clearance thus necessitating access facilitation pruning.
- b) Material which will contaminate the soil, e.g. concrete mixings, diesel oil and vehicle washings, should not be discharged within 10 metres of the tree stem.
- c) Fires should not be lit in a position where their flames can extend to within 5 m of foliage, branches or trunk. This will depend on the size of the fire and the wind direction.
- d) Notice boards, telephone cables or other services should not be attached to any part of the tree.
- e) It is essential that allowance should be made for the slope of the ground so that damaging materials such as concrete washings, mortar or diesel oil cannot run towards trees.

9.0 Supervision

- 9.1 Most damage to trees on developments sites is caused inadvertently and to ensure continued protection during development a system of site monitoring is proposed.
- 9.2 Basic checks will ensure that protective fencing remains intact. Any unforeseen issues can also be identified and discussed before damage to the tree(s) occurs.
- 9.3 The Local Planning Authority may secure the following schedule by way of Planning Condition. To be effective the Local Planning Authority must provide us with a copy of the formal Decision Notice to ensure we can then contact and follow up the proposed monitoring. A copy of the Decision Notice should be emailed to enquiries@arbconsultants.co.uk The number of proposed visits is driven by the scale of the proposal
- 9.4 A more detailed explanation of what will be assessed during the proposed monitoring visits is contained in Appendix

Visit	Date	Status
Pre-commencement Inspections Attend site to inspect type and location of tree protection and any temporary ground protection prior to development commencing and discuss any issues associated with demolition/ enabling works	TBC	Incomplete
Site Inspection Attend site to confirm fencing remains in place and supervise etc.	TBC	Incomplete
Site Inspection Attend site to confirm fencing remains in place and supervise etc.	TBC	Incomplete
Site Inspection Attend site to confirm fencing remains in place and supervise etc.	TBC	Incomplete
Site Inspection Final site visit to confirm that no damage has been done to retained trees/ identify any remedial actions in the event damage has occurred. Assess any required tree surgery following construction	TBC	Incomplete


10.0 Conclusion and Impact Statement

- 10.1 Trees within and adjacent to the proposed site and compliant with the scope of the development have been assessed in accordance with BS:5837:2012.
- 10.2 Some of the trees afford amenity through their function as a screen and a softening of the landscape.
- 10.3 Forty three individual trees, one group and 2 shrub groups have been assessed in response to the proposed development. It is anticipated that trees T23 to T26, T33, T34, T41 to T44, need to be removed to facilitate development. Therefore the arboricultural impact by the development will be not insignificant but all the trees to be removed are category C and none have a significant impact on amenity. Although some trees require removal the losses should be mitigated with new planting so as to improve the arboricultural population.
- 10.4 The impact of the proposed development has been assessed and in our professional opinion provided that the works take place in accordance with the method statements specified and replanting appropriately the works will not be detrimental to the retained trees and the overall arboricultural population will increase.
- 10.5 No work shall commence on site until such time as this method statement has been submitted to and approved in writing by the Local Planning Authority. All retained trees on the site shall be protected from damage as a result of the works on site, to the satisfaction of the Local Planning Authority in accordance with its guidance notes and relevant British Standards (e.g. BS5837:2012) or the duration of the development. In the event that trees become damaged during construction, the Local Planning Authority shall be notified and remedial action agreed and implemented. In the event that any tree(s) dies or is removed without the prior consent of the Local Planning Authority, it shall be replaced within the first available planting season, in accordance with details agreed with the Local Planning Authority.
- 10.6 All technical issues relating to arboriculture should be addressed to Arbconsultants Ltd in the first instance. Arbconsultants Ltd will liaise between the Local Planning Authority and any interested parties. It is suggested that the development proceeds in accordance with the above recommendations.


Appendix 1 Site Location

Hibaldstow


MR. P. FOX
LAND NORTH OF CASTLEFIELD HOUSE
121 STATION ROAD
HIBALDSTOW
BRISG DN20 9DU

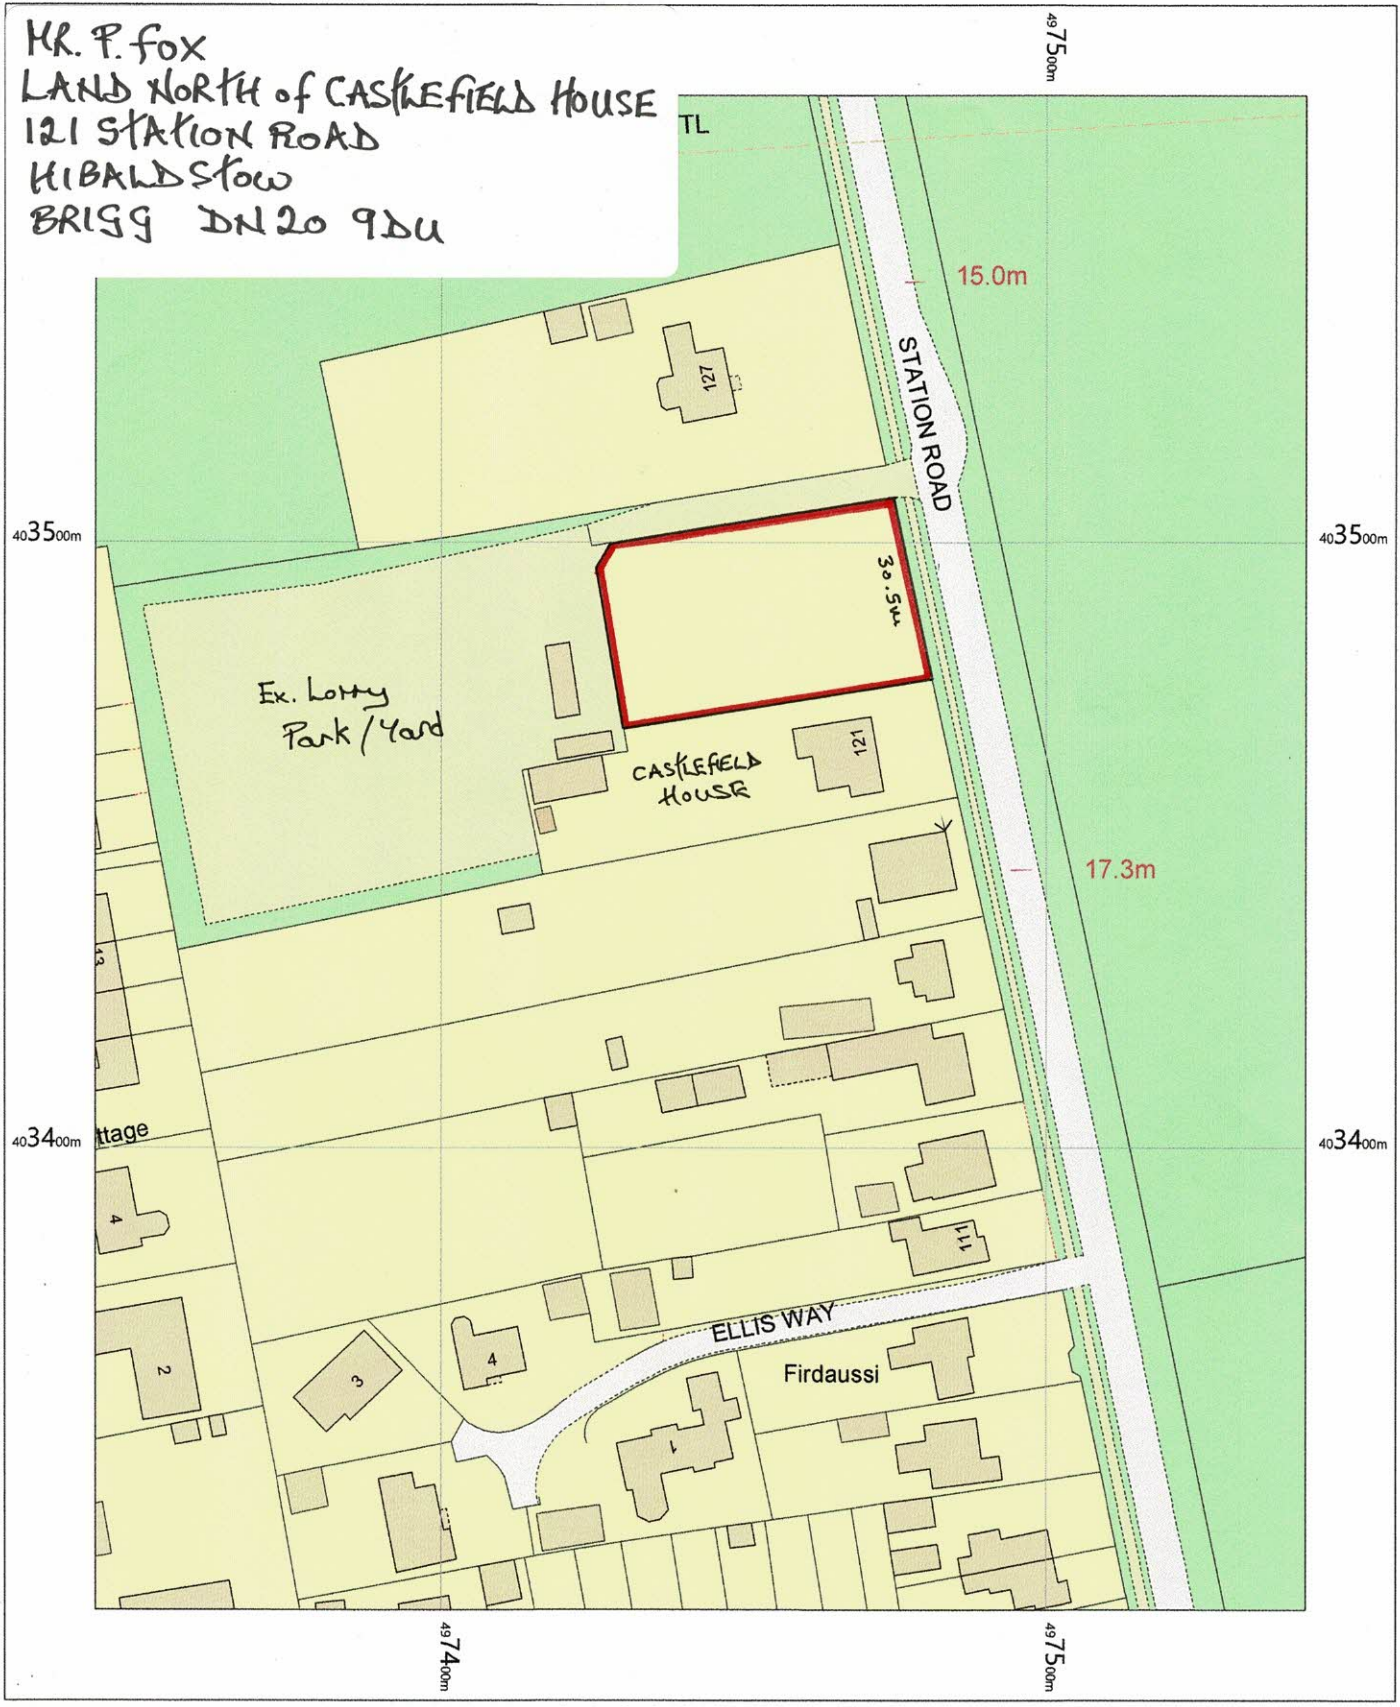

"LOCATION PLAN"




DRS. No. PF/21/01



Monday, July 19, 2021, ID: BW1-00977844
maps.blackwell.co.uk

1:1250 scale print at A4, Centre: 497443 E, 403449 N

©Crown Copyright and database rights 2021 OS Licence no. 100041041



BLACKWELL'S
MAPPING SERVICES
PERSONAL & PROFESSIONAL MAPPING
www.blackwellmapping.co.uk


TEL: 0800 151 2612
maps@blackwell.co.uk



Appendix 2 Tree Survey Data Tables


Tree number	Species	Diameter (cm)	Height	Spread North	Spread East	Spread South	Spread West	Height above ground of first branch over field	Life stage	General observations	Safe useful life	.Category	Recommendation
1	Birch	54*	19	6	3	7	3	8N	M	Dense ivy into crown precludes full VTA. Wires through crown. Minor dead wood.	20 to 40	B	Sever ivy and reinspect - Protect with barriers
2	Horse Chestnut	70*	18	6	3	6	6	2N	M	Leaf minor throughout crown. Some canker to main stem. Minor dead wood.	20 to 40	B	Monitor annually - Protect with barriers
3	Ash	65*	19	7	5	8	8	3N	M	Third party tree. No evidence of Ash Dieback at present, but some minor dead wood.	20 to 40	B	Monitor annually - Protect with barriers
4	Monkey Puzzle	15*	4	2	2	2	2	0	Y	Young tree in good condition.	20 to 40	B	Protect with barriers
5	Irish Yew	20 m/s	4	2	2	2	2	0.5	SM	Semi-mature tree in good condition.	20 to 40	B	Protect with barriers
6	Sycamore	78	20	8	6	5	8	6N	M	Multi-stemmed at 5m with some inclusions. Minor dead wood. Close to T7	20 to 40	A	Monitor annually - Protect with barriers
7	Lime	52*	20	3	4	3	3	0	M	Dense epicormic from ground level into crown precluded full VTA. Minor dead wood. Suppressed by T6 and T8.	20 to 40	B	Sever epicormic and reinspect — Protect with barriers
8	Sycamore	62	19	5	9	9	8	8E	M	Some ivy into crown. Moderate dead wood. Asymmetric crown.	20 to 40	B	Sever ivy and reinspect. Crown clean - Protect with barriers
9	Horse Chestnut	52	18	5	3	8	8	2S	M	Leaf minor throughout crown. Some canker to main stem. Minor dead wood.	20 to 40	B	Protect with barriers
10	Plum	22	4	1.5	1.5	1.5	1.5	2W	OM	Poor condition. Large snap out/lost leader - remaining wound has rot and cavity.Limited safe life expectancy.	<10	U	Fell
11	Plum	16	4	2	1	1	1	1S	M	Minor dead wood. Asymmetric crown.	10 to 20	C	Protect with barriers
12	Apple	19	5	2	5	4	2	1.8E	M	Die back. Dead wood. Wisteria in crown.	10 to 20	C	Monitor annually - Protect with barriers
13	Weeping Willow	10	4	4	4	4	4	0	SM	Semi-mature tree in good condition.	20 to 40	C	Protect with barriers
14	Cedar	25	8	2	3	3	4	1E	SM	Semi-mature tree in good condition.	20 to 40	B	Protect with barriers
15	Pine	24	6	3	2.5	3	3	1E	SM	semi-mature tree in reasonable condition. Some die back	20 to 40	C	Protect with barriers
16	Sycamore	64	19	8	8	8	6	1E	M	Crown lifted over property to rear. Twin stemmed at 2m. Minor dead wood.	20 to 40	B	Protect with barriers
17	Sycamore	26	8	3	3	3	3	4E	SM	Crown lifted over property to rear. Minor dead wood.	20 to 40	C	Protect with barriers
G18	Apple	50	2	1.5	1.5	1.5	1.5	0	M	2 trees topped/managed in past.	10 to 20	C	Protect with barriers
19	Sycamore	90*	20	8.5	9	9.5	8	2E	M	Twin stemmed at > 1.5m with inclusion. Minor dead wood. Lorry park (?) to rear and other building works in progress suggests earth works up to boundary along the rear.	20 to 40	B	Monitor annually - Protect with barriers
20	Apple	27	5	4	3	4	2.5	0	OM	Die back. Old pruning wounds with cavities. At point of limb removal there is a soft bracket fungi (old and decayed preventing identification)	10	C	Monitor annually - Protect with barriers
21	Copper beech	16	8	5	4	4	4	1S	SM	Semi-mature tree in good condition.	20 to 40	B	Protect with barriers
22	Rhus	8	5	2	2	2	2	1.5	Y	Young tree in good condition.	20 to 40	B	Protect with barriers
23	Holly	17	7	2	2	2	2	1S	SM	Suppressed. Die back. Thinning crown.	10 to 20	C	Fell to facilitate development
24	Pear	20*	8	2	3	2	2.5	0	M	Ivy/ Epicormic/ Minor dead wood.	20 to 40	C	Fell to facilitate development
25	Holly	2 x 20	6	2	2	2	2	1S	OM	Topped in past. Decay at pruning wounds. Thin crown. Suppressed.	10 to 20	C	Fell to facilitate development
26	Apple	57	7	6	6	3	3	1S	OM	Old pruning wounds with cavities. Epicormic. Minor dead wood.	10 to 20	C	Fell to facilitate development
H27	Leyland cypress with holly	10 m/s	7	1	1	1	1	0	EM	Maintained hedge	20 to 40	C	Protect with barriers
28	Pear	20*	8	2	3	2	3	2E	M	Tree located in dense planting. Suppressed poor form. Low landscape value.	10 to 20	C	Protect with barriers
29	Pear	20*	8	2	2.5	2	3	7W	M	Tree located in dense planting. Suppressed poor form. Low landscape value.	10 to 20	C	Protect with barriers
30	Yew	18	7	3	1	2	3	1W	EM	Tree located in dense planting. Suppressed poor form. Low landscape value.	20 to 40	C	Protect with barriers
31	Lime	75*	19	7	8	8	7.5	7W	M	Dominant tree on road side. High landscape value. Dense epicormic restricting full VTA.	20 to 40	A	Sever epicormic and reinspect — Protect with barriers - Cellular Confinement System
32	Hawthorn	38*	7	3	3	2	3	2E	M	Old boundary tree. Poor form and low vigour. Leaning over road. Suppressed.	10 to 20	C	Protect with barriers
33	Hawthorn	34*	7	3	3	3	3	2E	M	Old boundary tree. Poor form and low vigour. Leaning over road. Suppressed.	10 to 20	C	Fell to facilitate development
34	Apple	15	3	1	1	1	1.5	1W	EM	Topped in past. Suppressed low value landscape tree.	10 to 20	C	Fell to facilitate development
35	Purple leaved plum	20 m/s	7	3	1	1	4	2W	M	Suppressed. Poor form. Low value amenity tree	10 to 20	C	Protect with barriers
36	Plum	15 m/s	7	2	5	2	1	2E	M	Suppressed. Poor form. Low value amenity tree	10 to 20	C	Protect with barriers
37	Rowan	24 m/s	6	1	5	4	3	2E	M	Suppressed. Poor form. Low value amenity tree	10 to 20	C	Protect with barriers
38	Holly	31	7	2	2	1	3	1W	M	Suppressed. Poor form. Low value amenity tree	10 to 20	C	Protect with barriers
39	Yew	50*	9	3	3	3.5	3	0	M	Maintained regularly	20 to 40	B	Protect with barriers
40	Laburnum	19 & 22	7	2	4	2	1	4S	OM	Nearly dead. Very little live growth	<10	U	Fell
41	Apple	49	10	4.5	5	5	4	1N	M	Old pruning wounds with cavities. Epicormic. Minor dead wood.	10 to 20	C	Fell to facilitate development
42	Lawson Cypress	35*	9	2	2	2	2	0	M	Mature tree. Moderate form	20 to 40	C	Fell to facilitate development
43	Plum	40*	8	2	3	3	3	1.5E	M	Large snap out. Dead wood. Die back	10 to 20	C	Fell to facilitate development
44	Plum	34	8	3	2	4	3	2N	M	Some die back some dead wood. Old pruning wounds with small cavities	10 to 20	C	Fell to facilitate development
SG1	Mixed species	5	2	1	1	1	1	1	M	Species include; Aucuba, laurel, snow berry, mock orange, privet	10 to 20	C	Protect with barriers except 6m section to be removed
SG2	Mixed species	5	2	1	1	1	1	1	M	Species include; lilac, laurel, snow berry, mock orange, privet	10 to 20	C	Protect with barriers

Appendix 3 Tree Survey Plan

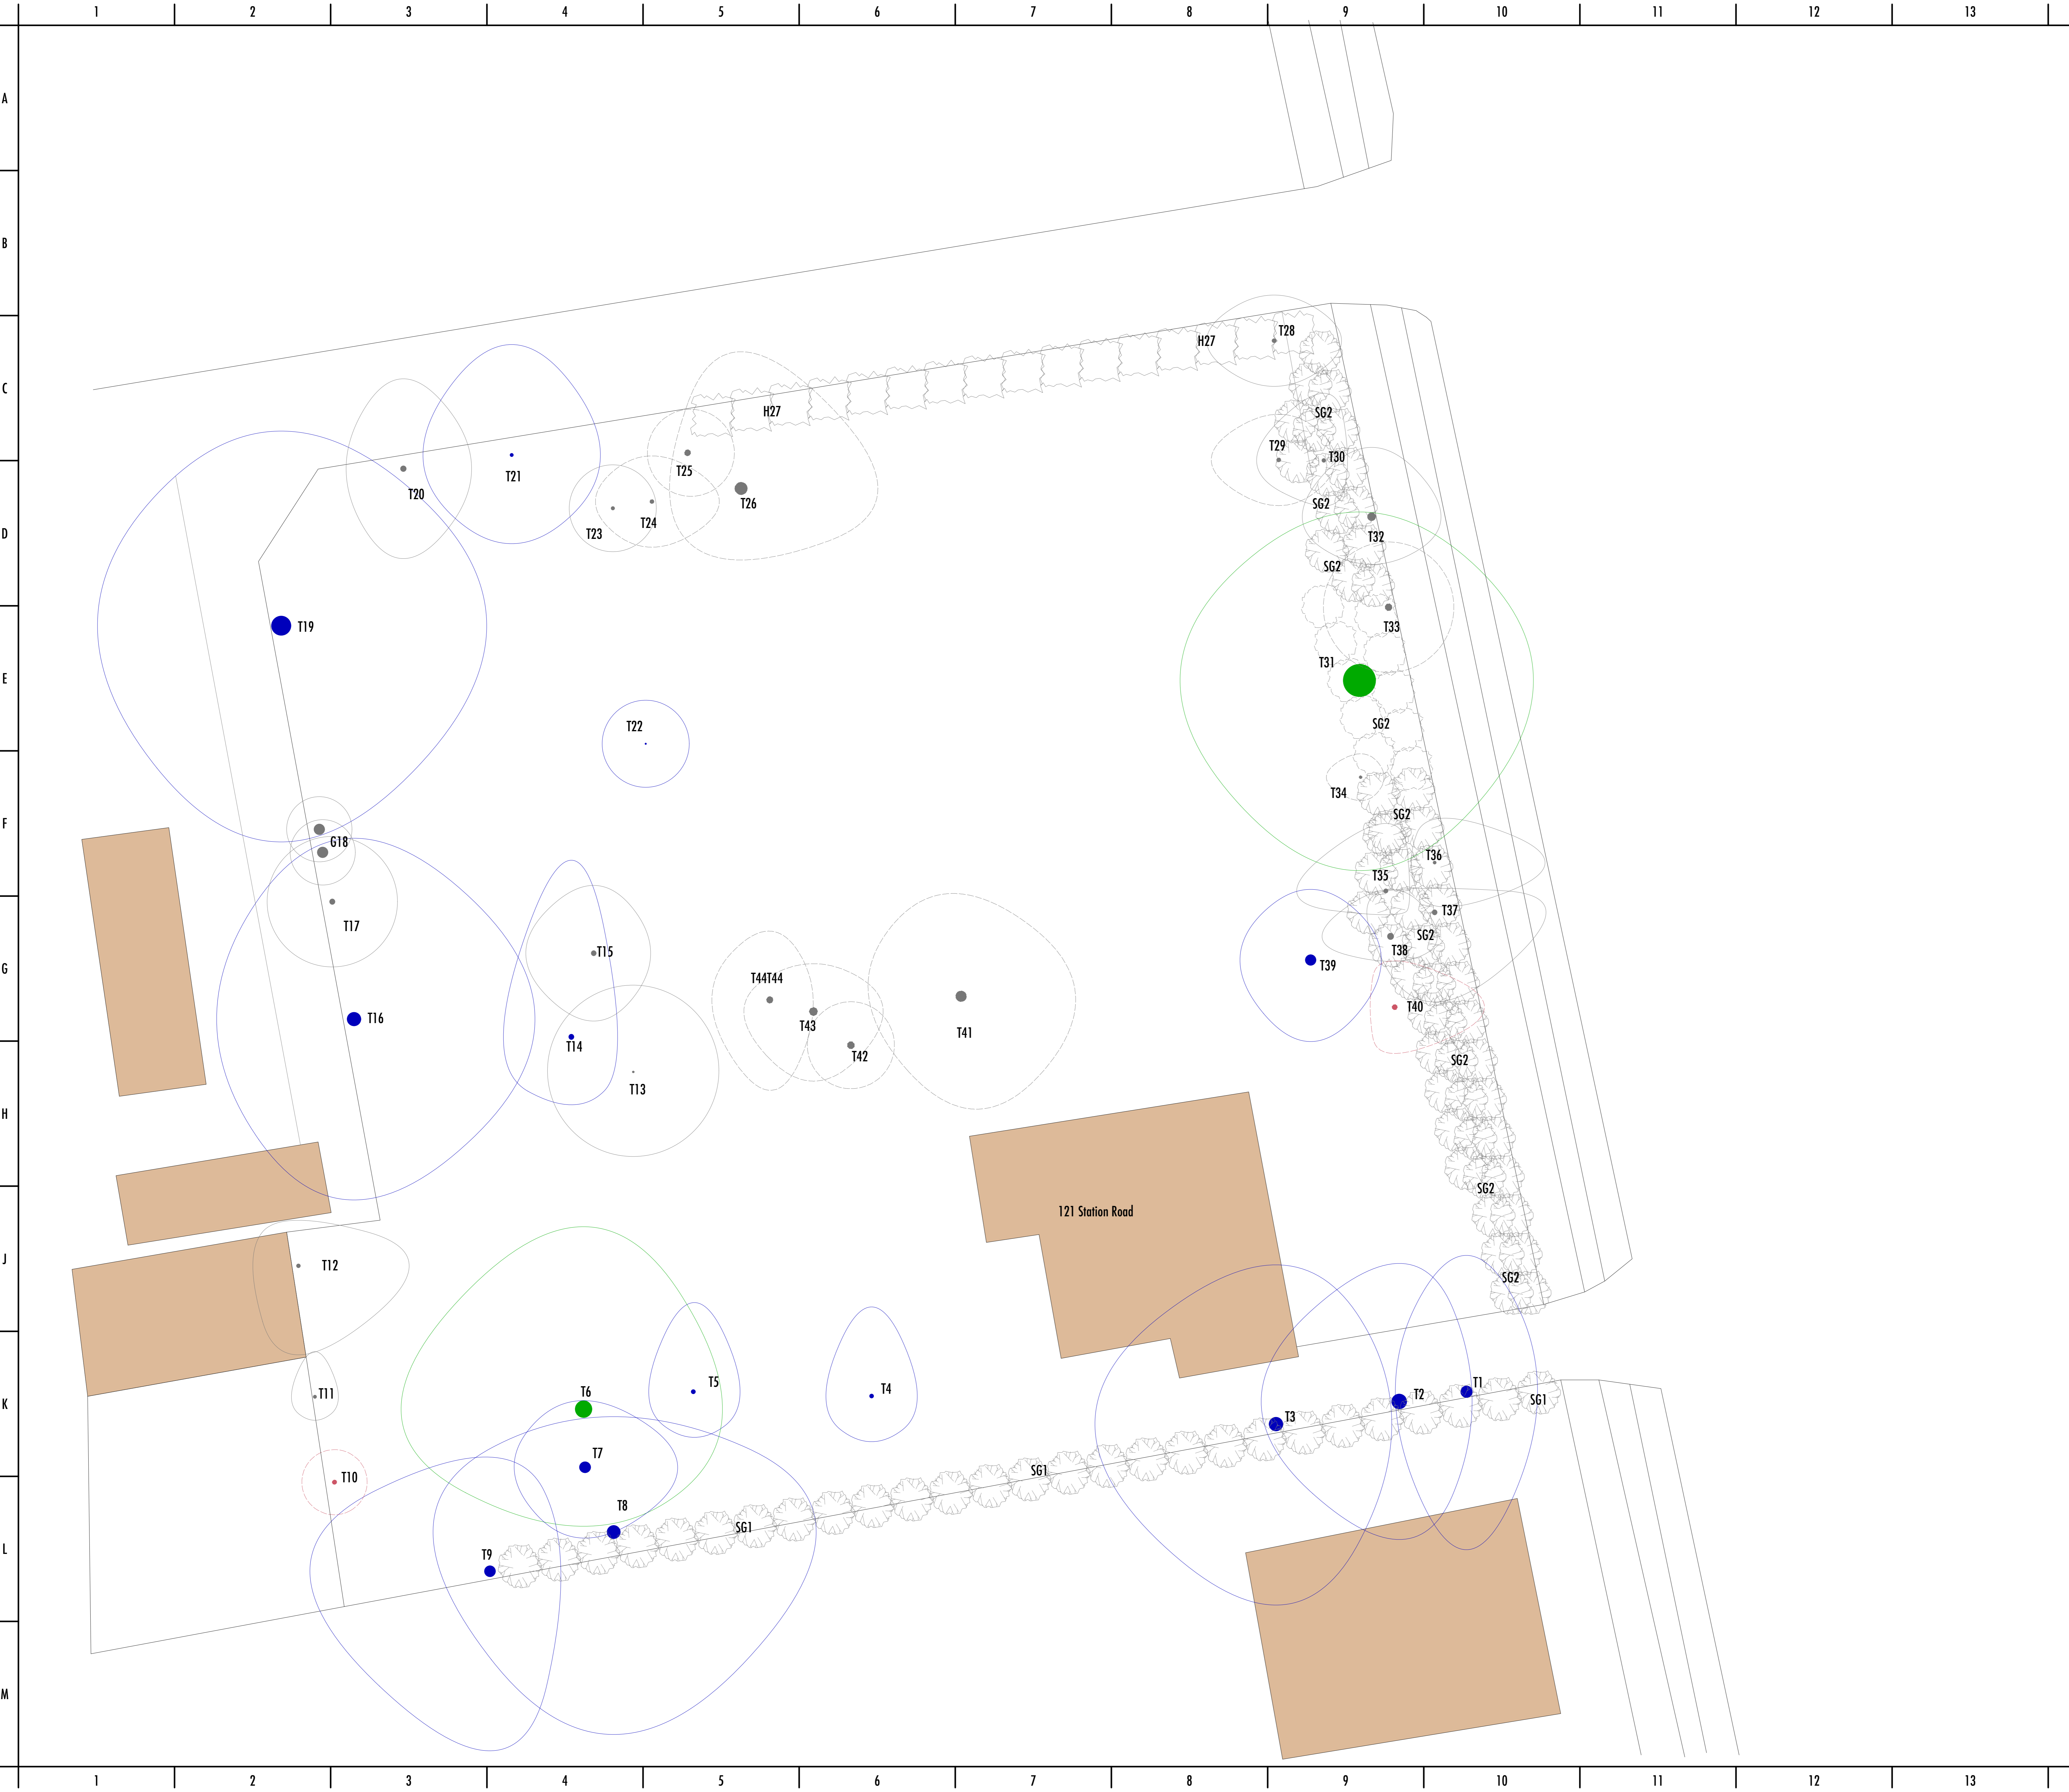

No.	Date	Appr	Revision Notes
			<ul style="list-style-type: none"> ○ Category U Retained ⊖ Category U Removed ○ Category A Retained ⊖ Category A Removed ○ Category B Retained ⊖ Category B Removed ○ Category C Retained ⊖ Category C Removed Ground Protection Barrier Protection Cellular Confinement System Specialist foundation Root Protection Area Retained Root Protection Area Felled

No.	Date	Issue Notes



Design Firm
Arbconsultants Ltd
 Myerscough College
 Bilsborrow
 Lancashire PR3 0RY

Consultant
Dr John Graham

Project Title
BS5837 2012 AIA

Sheet Title
Appendix 3 Tree Survey Plan


Project Manager	J Mumby	Project ID	121 Station Road
Drawn By	CR	Scale	1:100 @ A0
Reviewed By	JG	Sheet No.	Sht-1
Date	Date		of
CAD File Name	JEM		4

Appendix 4 Tree Constraints Plan (TCP)

4.6.1 For single stem trees, the RPA (see 3.7) should be calculated as an area equivalent to a circle with a radius 12 times the stem diameter. For trees with more than one stem, one of the two calculation methods below should be used. In all cases, the stem diameter(s) should be measured in accordance with Annex C, and the RPA should be determined from Annex D. The calculated RPA for each tree should be capped to 707 m².


a) For trees with two to five stems, the combined stem diameter should be calculated as follows:

$$\sqrt{(\text{stem diameter } 1)^2 + (\text{stem diameter } 2)^2 \dots + (\text{stem diameter } 5)^2}$$

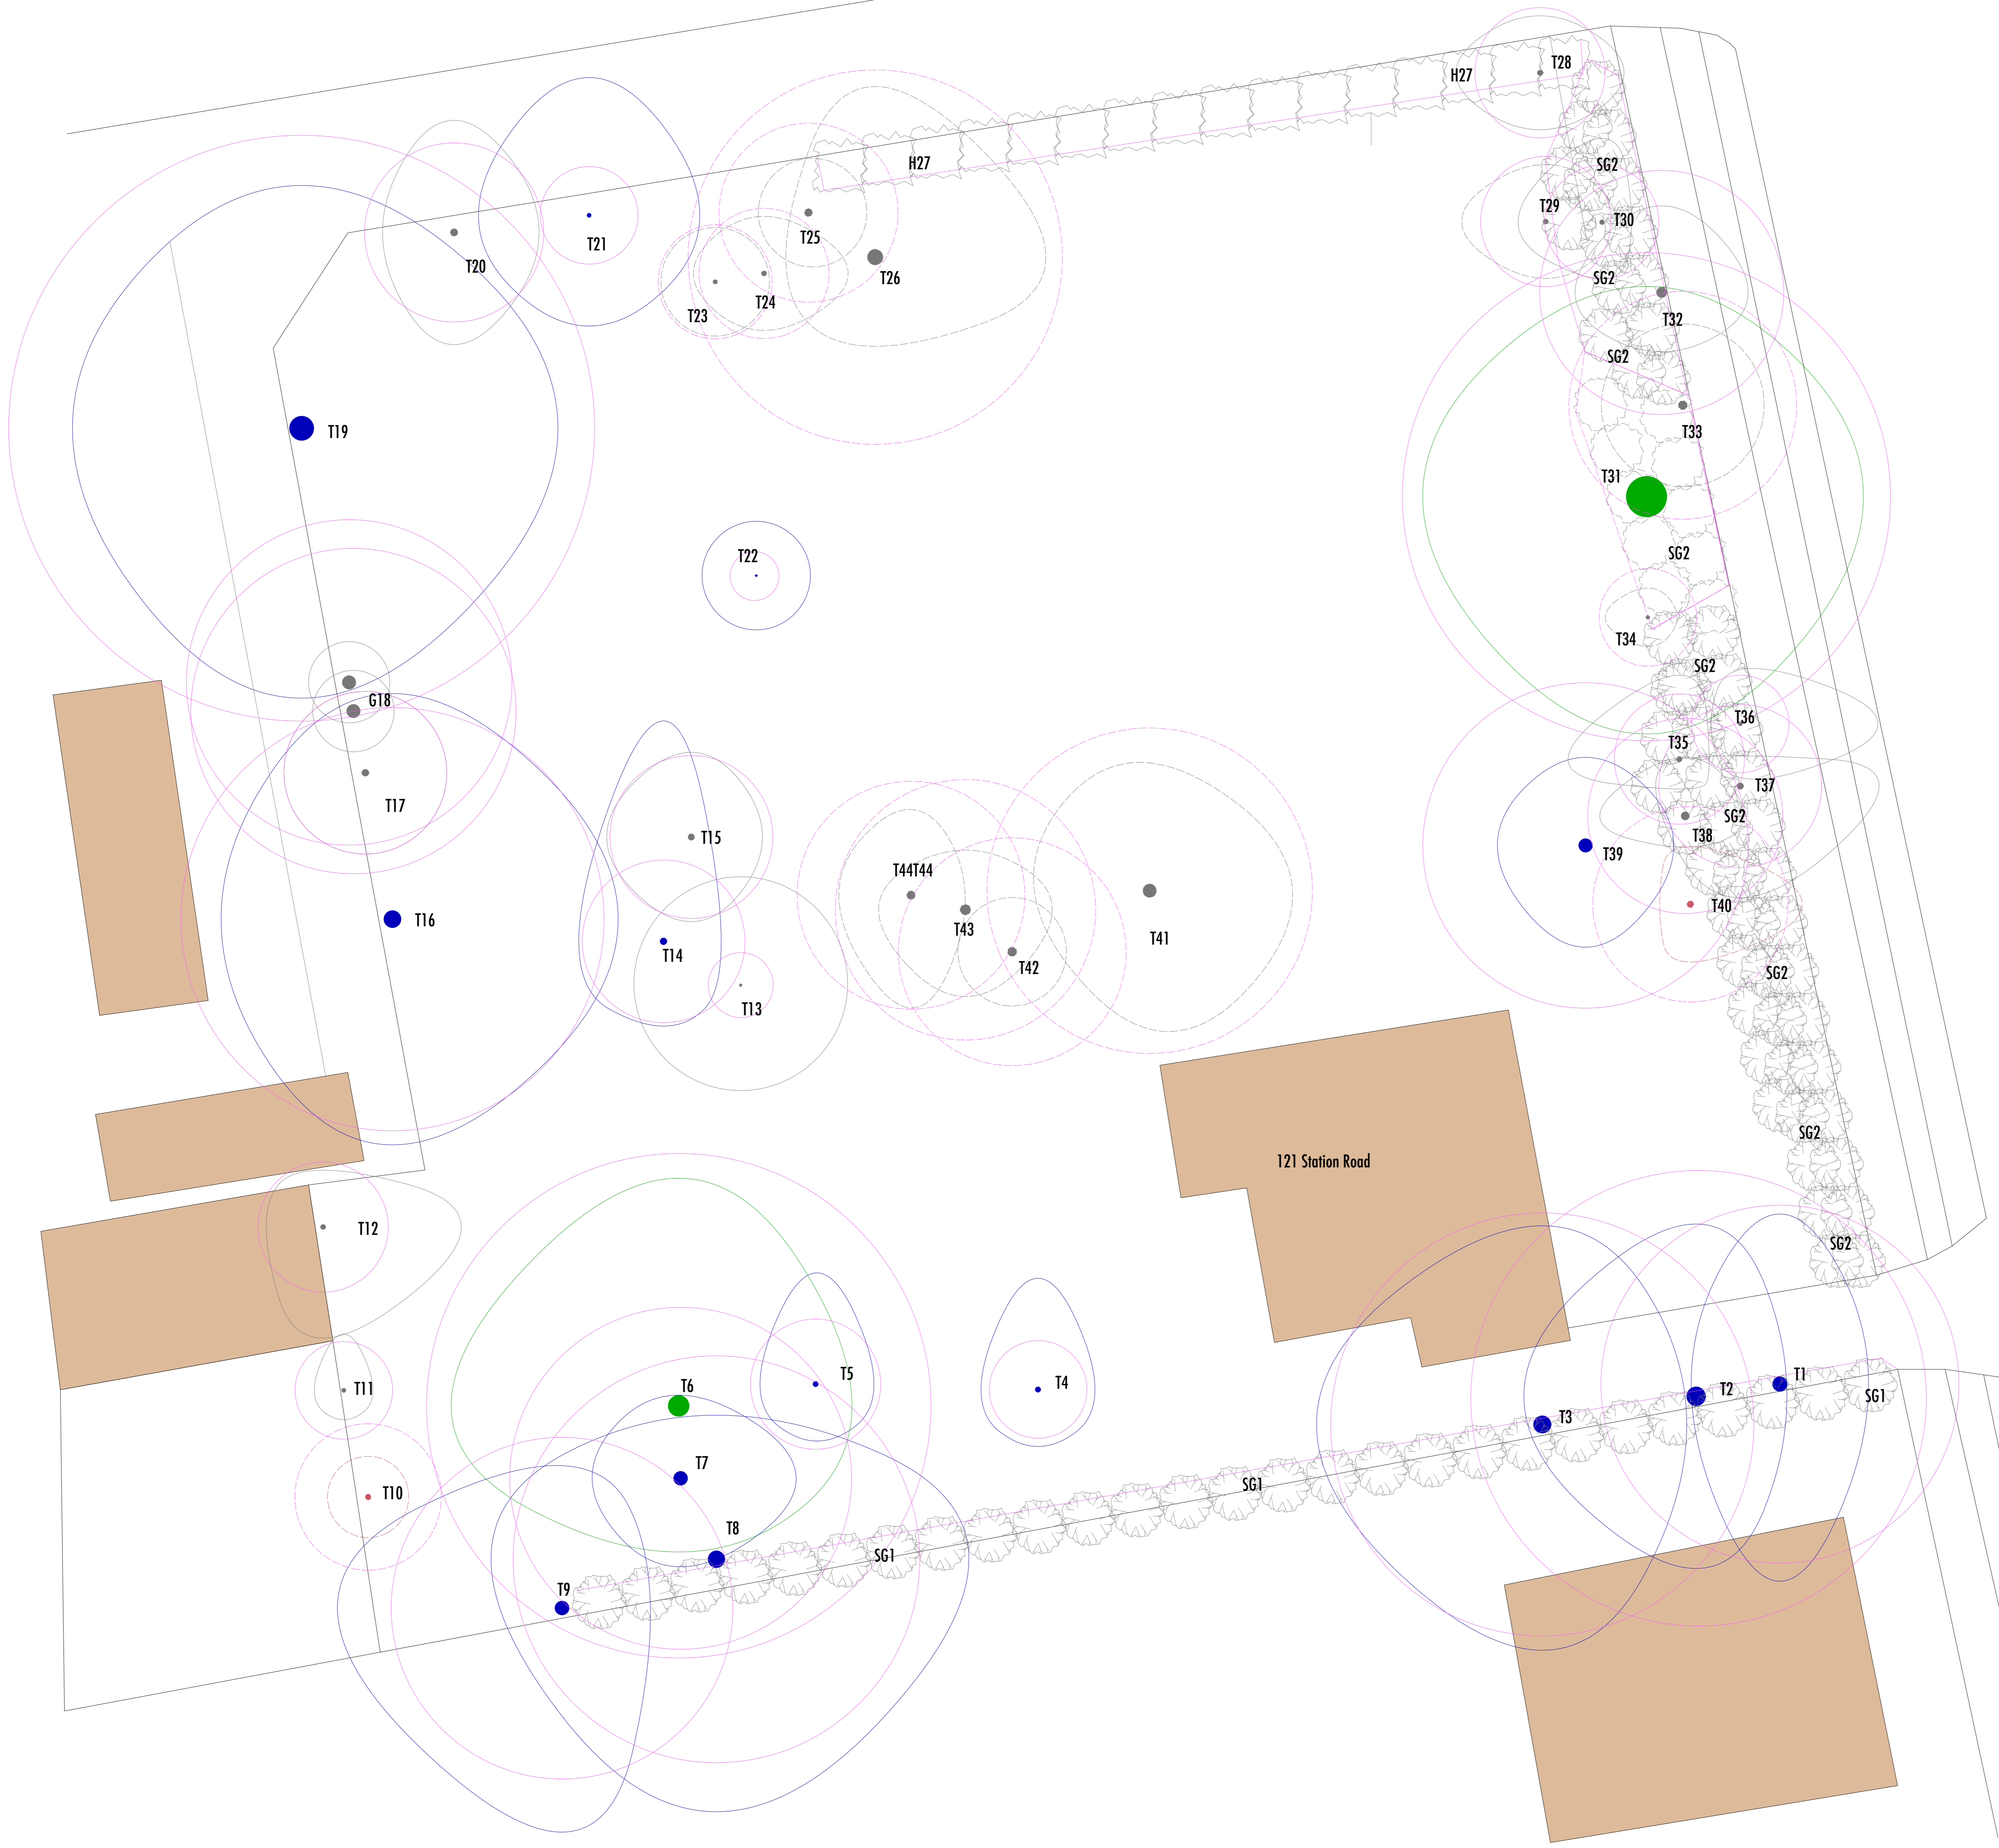

No.	Date	Appr	Revision Notes
			<ul style="list-style-type: none"> ○ Category U Retained ⊖ Category U Removed ○ Category A Retained ⊖ Category A Removed ○ Category B Retained ⊖ Category B Removed ○ Category C Retained ⊖ Category C Removed Ground Protection Barrier Protection Cellular Confinement System Specialist foundation ○ Root Protection Area Retained ⊖ Root Protection Area Felled

No.	Date	Issue Notes

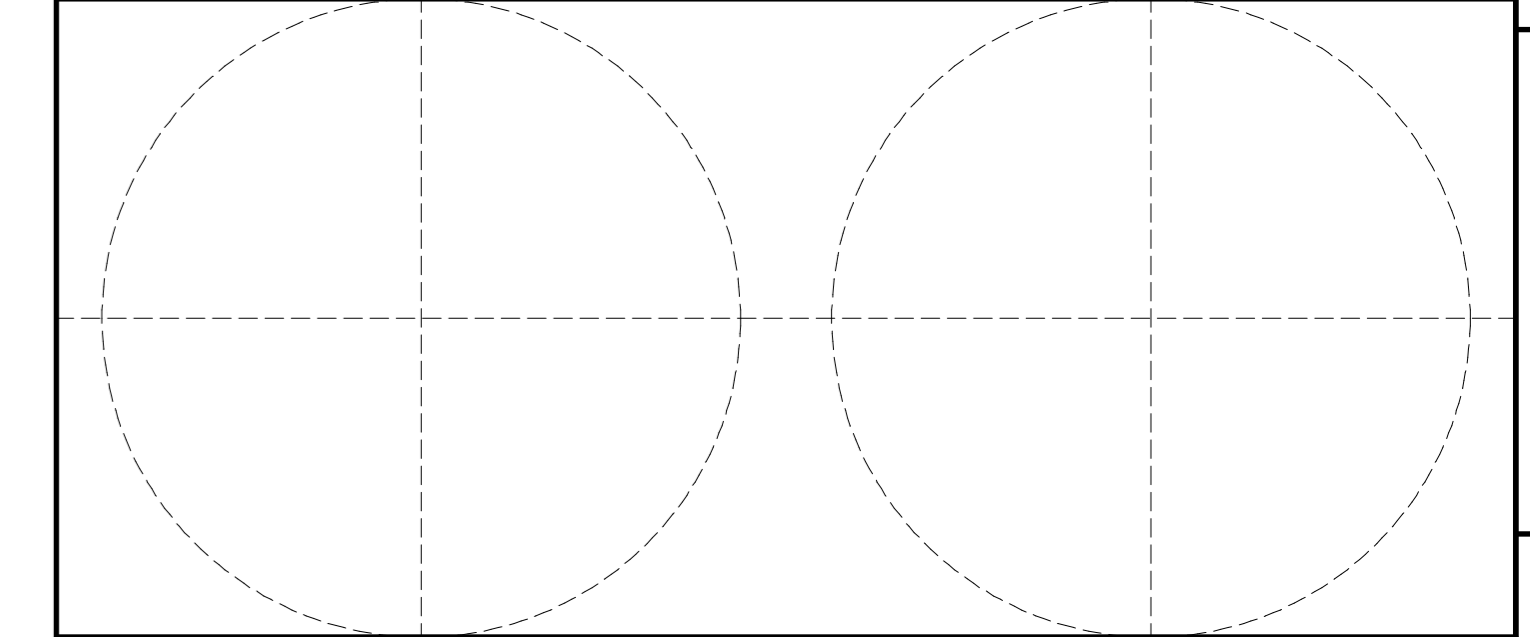

Design Firm
Arbconsultants Ltd
 Myerscough College
 Bilsborrow
 Lancashire PR3 0RY

Consultant
Dr John Graham

Project Title
BS5837 2012 AIA

Sheet Title
Appendix 4 Tree Constraints Plan

Project Manager	J Mumby	Project ID	121 Station Road
Drawn By	CR	Scale	1:100 @ A0
Reviewed By	JG	Sheet No.	Sht-2 of 4
Date	Date		
CAD File Name	JEM		

Appendix 5
Tree Protection Plan (TPP)

Appendix 6 RPA Calculations

September 2021				121 Station Road	
Tree ID	Single stem Diameter at 1.5m above ground level	No of stems (2-5)	No of stems 5 +	Root Protection Area (See Note)	Equivalent to a circle with a radius of
1	54*			6.6	137
2	70*			8.4	222
3	65*			7.8	191
4	15*			1.8	10
5	20 m/s			2.4	18
6	78			9.3	272
7	52*			6.3	124
8	62			7.5	177
9	52			6.3	124
10	22			2.7	23
11	16			1.8	10
12	19			2.4	18
13	10			1.2	5
14	25			3	28
15	24			3	28
16	64			7.8	191
17	26			3	28
G18	50			6	113
19	90*			10.8	366
20	27			3.3	34
21	16			1.8	10
22	8			0.9	3
23	17			2.1	14
24	20*			2.4	18
25		20 20 =28		3.3	34
26	57			6.9	150

H27	10 m/s			1.2	5
28	20*			2.4	18
29	20*			2.4	18
30	18			2.1	14
31	75*			9	255
32	38*			4.5	64
33	34*			4.2	55
34	15			1.8	10
35	20 m/s			2.4	18
36	15 m/s			1.8	10
37	24 m/s			3	28
38	31			3.6	41
39	50*			6	113
40		19 22 = 29		3.6	41
41	49			6	113
42	35*			4.2	55
43	40*			4.8	72
44	34			4.2	55
SG1	5			0.9	3
SG2	5			0.9	3

Root Protection Area (RPA) Calculator



arbconsultants

Appendix 7
Proposed / Combined

4.6.1 For single stem trees, the RPA (see 3.7) should be calculated as an area equivalent to a circle with a radius 12 times the stem diameter. For trees with more than one stem, one of the two calculation methods below should be used. In all cases, the stem diameter(s) should be measured in accordance with Annex C, and the RPA should be determined from Annex D. The calculated RPA for each tree should be capped to 707 m².


a) For trees with two to five stems, the combined stem diameter should be calculated as follows:

$$\sqrt{(\text{stem diameter } 1)^2 + (\text{stem diameter } 2)^2 \dots + (\text{stem diameter } 5)^2}$$

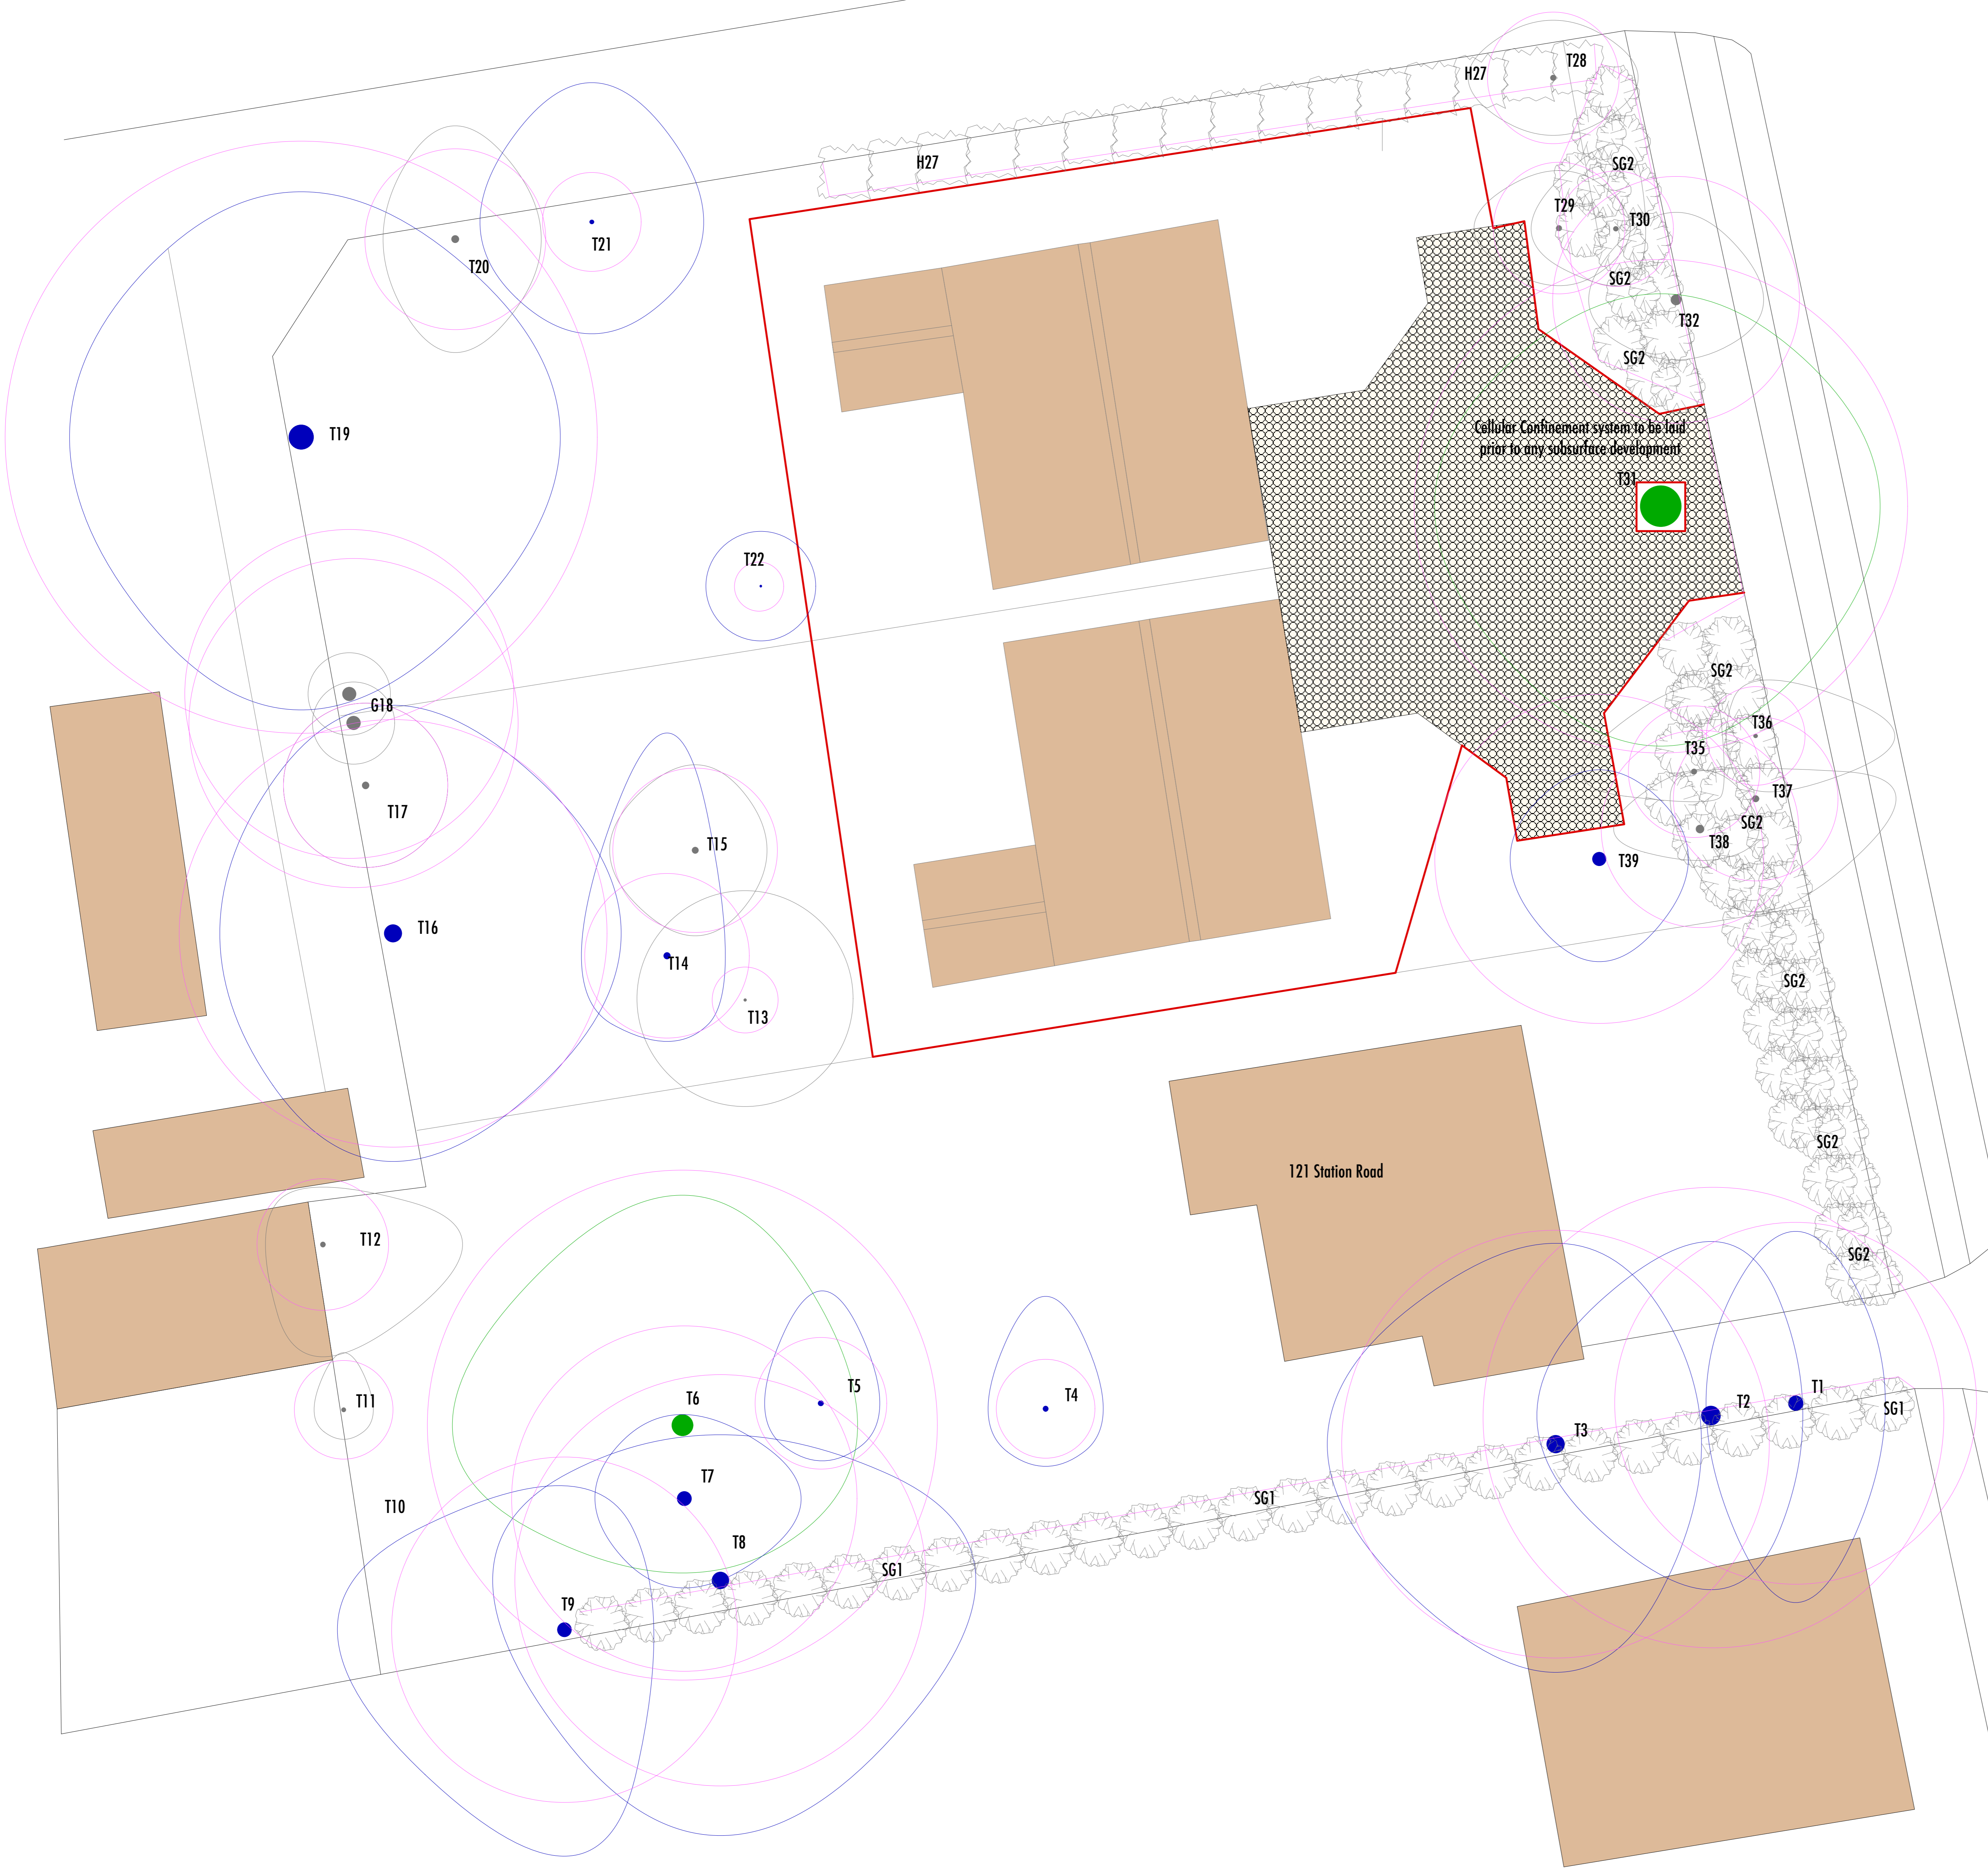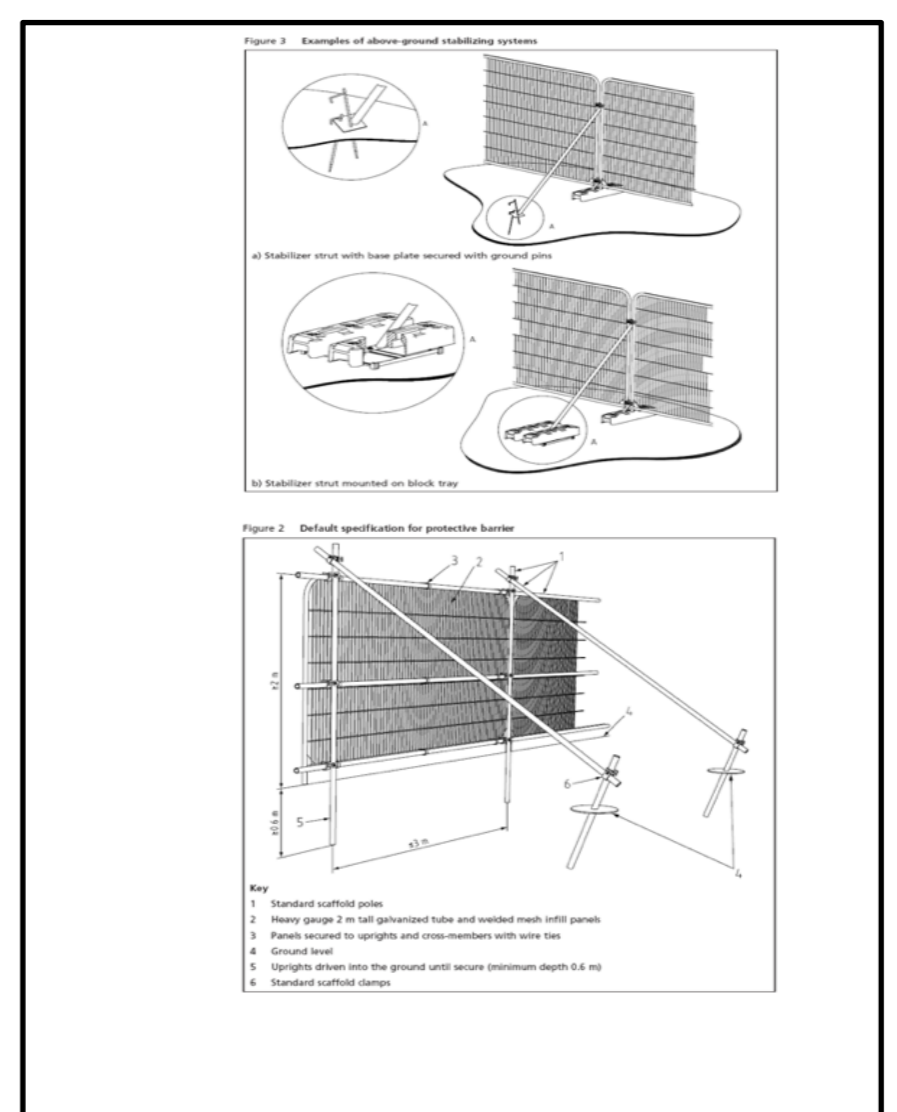

No.	Date	Appr	Revision Notes
			<ul style="list-style-type: none"> ○ Category U Retained ○ Category U Removed ○ Category A Retained ○ Category A Removed ○ Category B Retained ○ Category B Removed ○ Category C Retained ○ Category C Removed Ground Protection Barrier Protection Cellular Confinement System Specialist foundation Root Protection Area Retained Root Protection Area Felled

No.	Date	Issue Notes

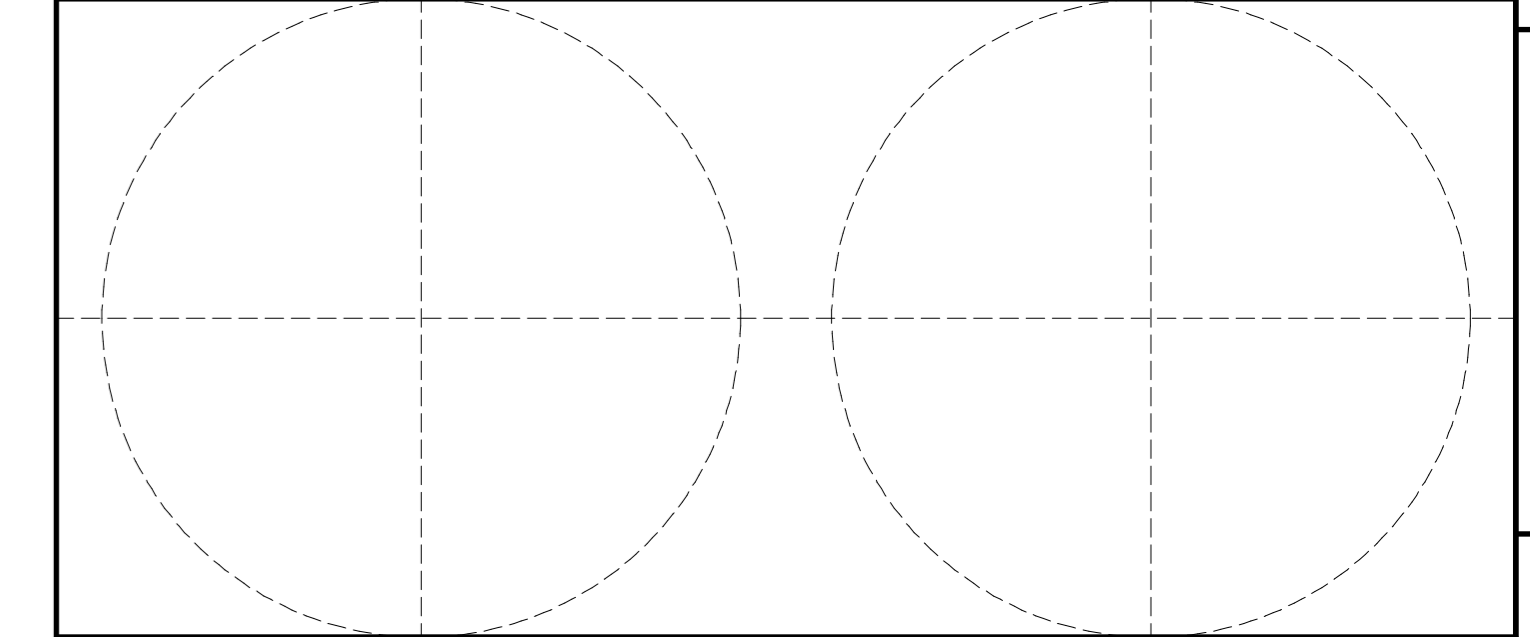

Design Firm
Arbconsultants Ltd
 Myerscough College
 Bilborough
 Lancashire PR3 0RY

Consultant
Dr John Graham

Project Title
BS5837 2012 AIA

Sheet Title
Appendix 7 Proposed / Combined

Project Manager	J Mumby	Project ID	121 Station Road
Drawn By	CR	Scale	1:100 @ A0
Reviewed By	JG	Sheet No.	Sht-4 of 4
Date	Date		
CAD File Name	JEM		
